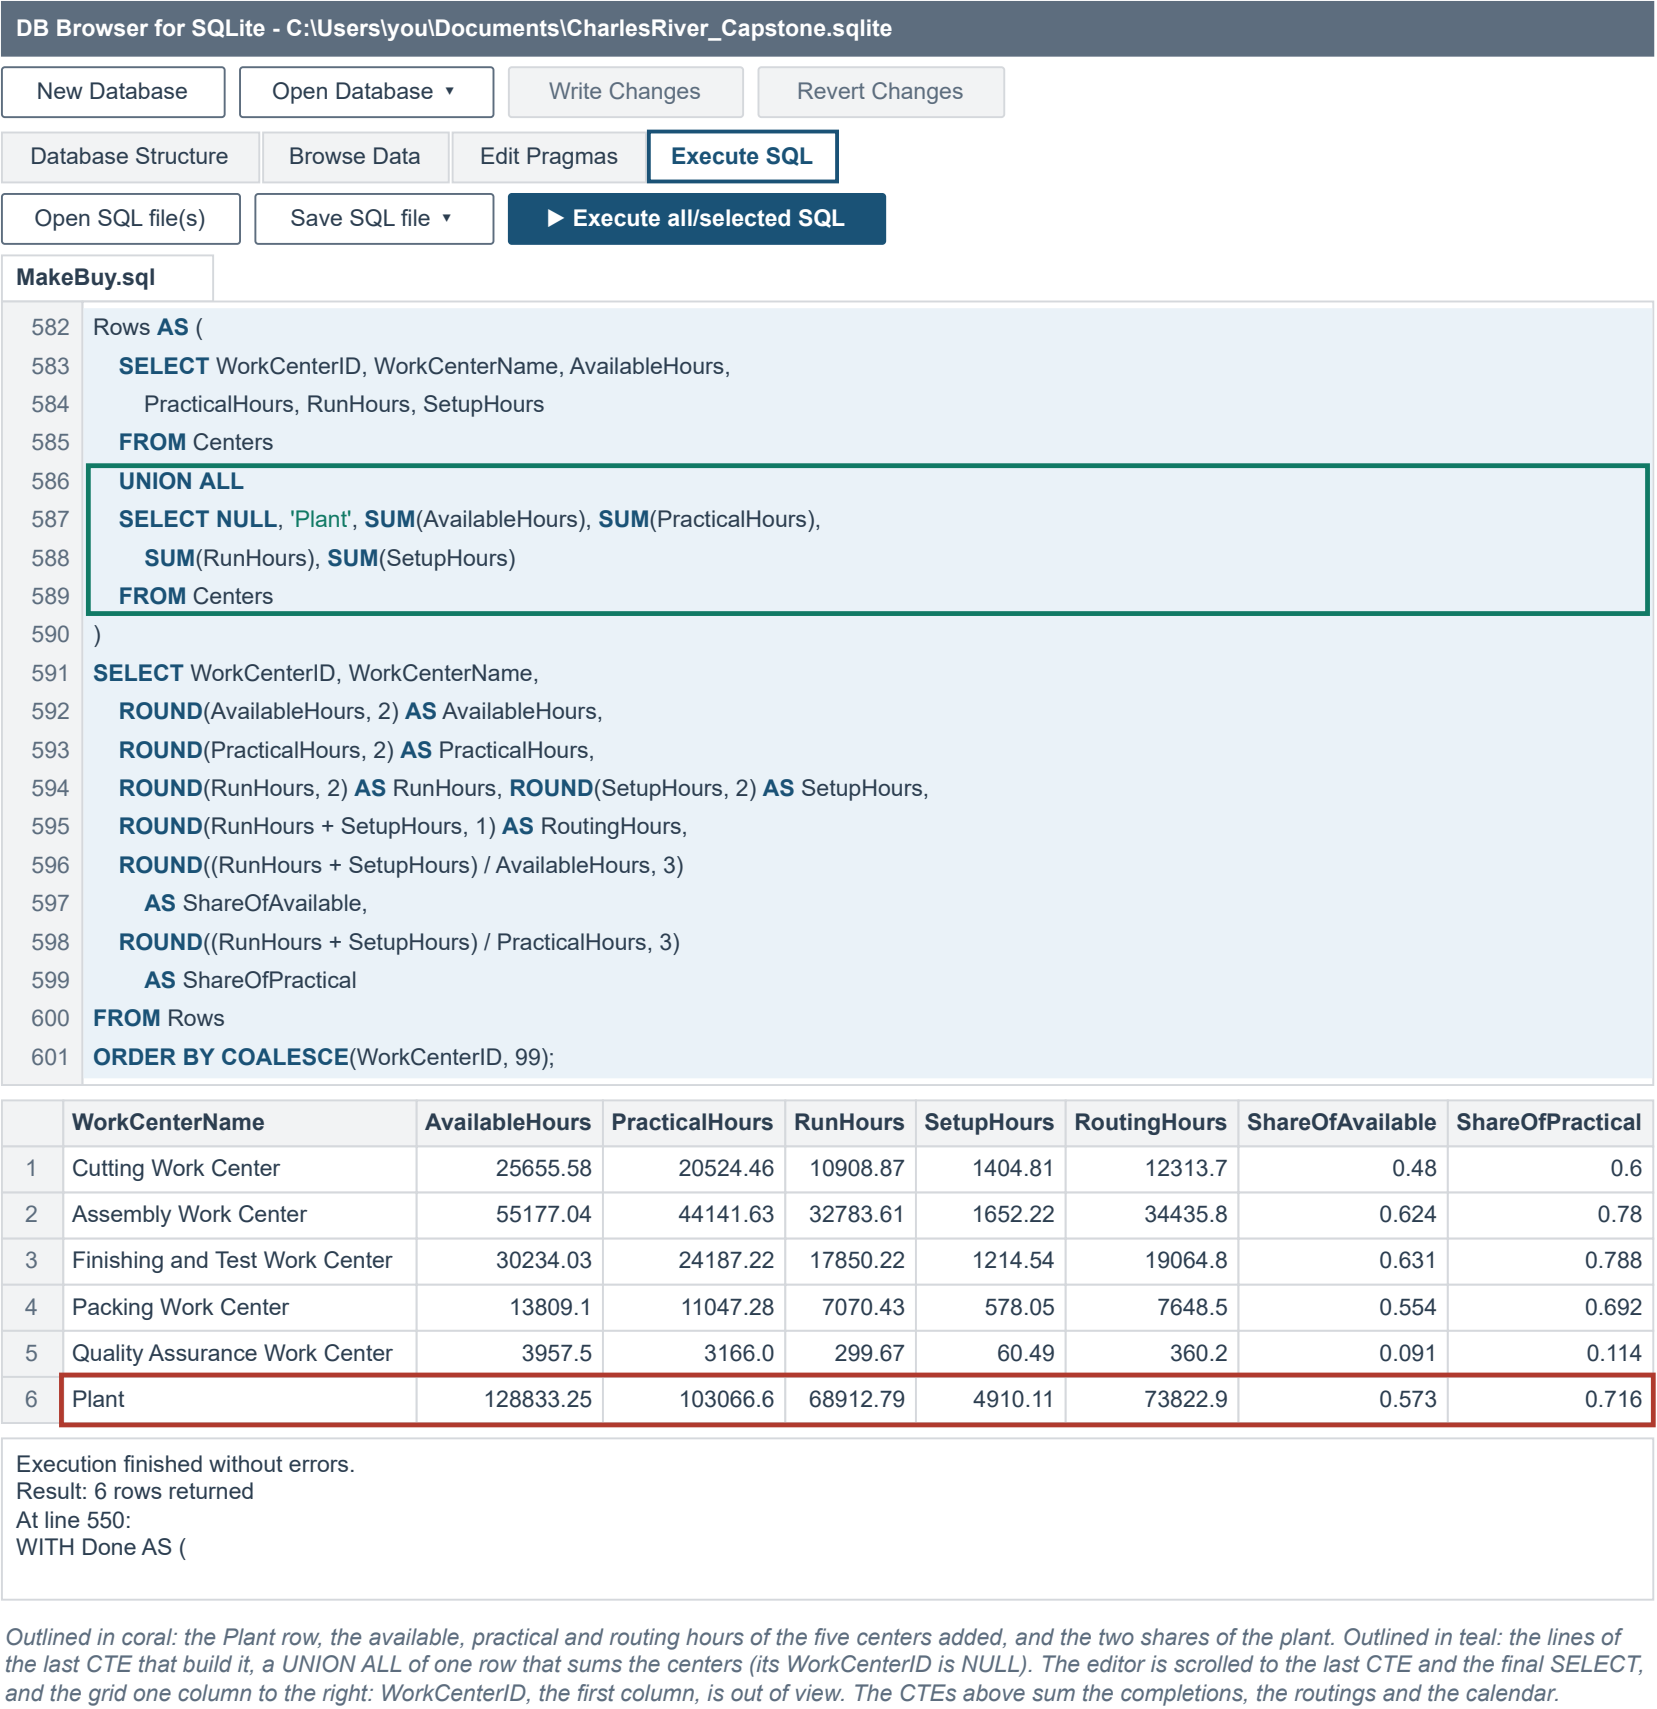


	WorkCenterName	AvailableHours	PracticalHours	RunHours	SetupHours	RoutingHours	ShareOfAvailable	ShareOfPractical
1	Cutting Work Center	25655.58	20524.46	10908.87	1404.81	12313.7	0.48	0.6
2	Assembly Work Center	55177.04	44141.63	32783.61	1652.22	34435.8	0.624	0.78
3	Finishing and Test Work Center	30234.03	24187.22	17850.22	1214.54	19064.8	0.631	0.788
4	Packing Work Center	13809.1	11047.28	7070.43	578.05	7648.5	0.554	0.692
5	Quality Assurance Work Center	3957.5	3166.0	299.67	60.49	360.2	0.091	0.114
6	Plant	128833.25	103066.6	68912.79	4910.11	73822.9	0.573	0.716

Outlined in coral: the Plant row, the available, practical and routing hours of the five centers added, and the two shares of the plant. Outlined in teal: the lines of the last CTE that build it, a UNION ALL of one row that sums the centers (its WorkCenterID is NULL). The editor is scrolled to the last CTE and the final SELECT, and the grid one column to the right: WorkCenterID, the first column, is out of view. The CTEs above sum the completions, the routings and the calendar.
